DELIVERABLES REPORT · QUARTERLY

CAF Compliance 12-Month Deliverables

What the ServiceNow ⇄ Salesforce integration project delivered in each quarter from February 2026, and what is planned for the quarter ahead.

Reporting window	February 2026 – January 2027
Delivered (actuals)	Q1 Feb–Apr · Q2 May–Jul · Q3 Aug–Oct (to 22 Oct)
Planned (forecast)	Q4 Nov 2026 – Jan 2027
Source	caf-sf-integration repository, main @ 571386c
Date	22 October 2026

1. Executive summary

The project set out to give application owners and approvers a Salesforce experience for CAF compliance while ServiceNow stays the system of record. Over three delivered quarters it has gone from an empty repository to a working, tested two-way integration with four Salesforce screens, a six-resource ServiceNow API, drift detection, durable callout logging and a three-level test pack.


193
commits on main (excluding merges)

39
pull requests merged (October)

289
files under version control

3
named contributors, plus the Reyantech org account

Quarter	Theme	Headline deliverables	Status
Q1 Feb–Apr 2026	Foundation and build	Design document; Salesforce data model; 5 Apex services; 4 Lightning components; ServiceNow outbound sync	Delivered
Q2 May–Jul 2026	Integration API and test harness	Outbound push rules; 6 inbound REST resources; Playwright harness; 139 test cases; Word evidence packs	Delivered
Q3 Aug–Oct 2026	Hardening and new screens	Decks; ServiceNow rebuilt on a new instance; Approvals, Reports, Admin screens; callout log; custom-metadata config; Apex and LWC unit tests	Delivered · deploy pending
Q4 Nov 2026–Jan 2027	Production readiness	Org deployment; CafSyncHealth tests; named approver; queued delivery; scheduled Sync Health; JWT	Planned

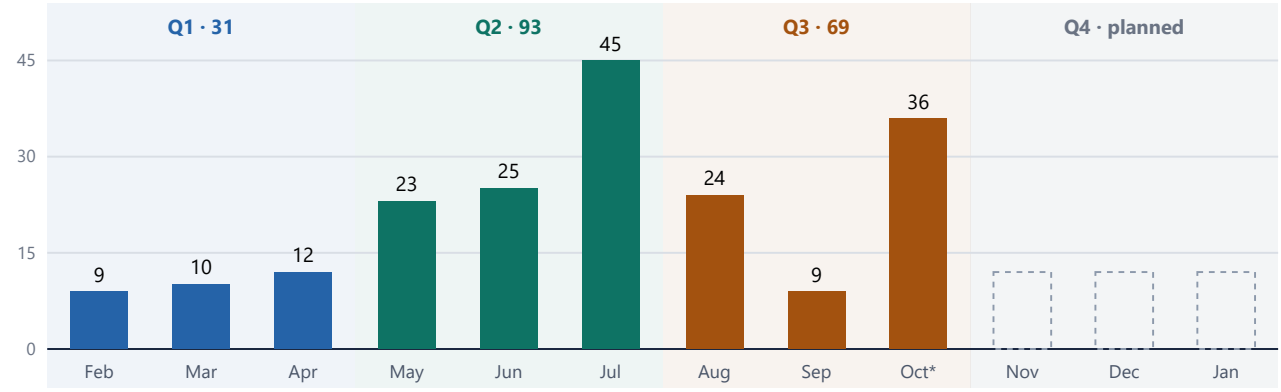

Commits per month on main, excluding merge commits, by author date. *October is a part month. Q4 outlines are placeholders, not a forecast of volume.

Figure 1 · Delivery activity by month and quarter

2. Milestone timeline



Figure 2 · Key milestones, by commit date on main

3. Q1 · February – April 2026

Q1 **Foundation and build** · 31 commits · 1 contributor

The quarter established the design and built the bulk of the Salesforce application and the start of the ServiceNow outbound sync.

Workstream	Deliverable	Status
Discovery and design	Repository scaffold, README and scope; technical design document with integration diagram; instance details; discovery handoff notes; security model section	Delivered
Salesforce data model	`CAF_Control_Catalog__c`, `CAF_Request__c`, `CAF_Task__c`; package manifest; `CAF_Integration` permission set; page layouts and tabs	Delivered
Apex services	`CafTaskService`, `CafEvidenceService`, `CafAttestationService`, `CafDashboardController`, `CafSyncHealth`; orphan-task clean-up script	Delivered
Lightning UI	`cafDashboard` compliance grid; `cafEvidence` upload and lists; `cafAttestation` approver flow; `cafSyncHealth` drift panel	Delivered
ServiceNow outbound	`CAFSalesforceSync` script include; `caf_short_desc` helper; business rule pushing controls to Salesforce	Delivered
Documentation	Salesforce deployment notes; session handoff updates	Delivered

Outcome

By the end of April the Salesforce side could render the compliance grid from mirrored data and the outbound sync could push the control catalogue. The inbound API that the Salesforce actions depend on was still to be built.

4. Q2 · May – July 2026

Q2 **Integration API and test harness** · 93 commits · 4 author accounts

The busiest quarter by volume. It completed the two-way contract and built the test and evidence machinery that proves both platforms agree.

Workstream	Deliverable	Status
ServiceNow outbound	Business rules to push requests and to retire deleted controls	Delivered
ServiceNow inbound API	Scripted REST resources: sync snapshot, update task, upload evidence, list evidence, attest task, resync record	Delivered
Configuration guide	ServiceNow setup guide, verified behaviour, inbound contract, known gaps	Delivered
Test harness	Playwright project with Salesforce and ServiceNow projects; storage-state auth; Lightning page objects; Salesforce, ServiceNow and CAF API helpers; watch mode; single-case runner	Delivered
Test data	Seed definitions for the demo estate, volume seed, connectivity probe, record-numbering repair	Delivered
Test suites	Outbound ETL, inbound UI, read-only, negative-path and regression, ServiceNow case suite	Delivered
Test catalogues	70 integration cases and 69 ServiceNow cases, with coverage summaries and run instructions	Delivered
Evidence	Case-result parser, branded per-case Word evidence packs, HTML evidence report, results for each suite	Delivered

Outcome

The integration contract was complete in both directions, and every executed case produced a Word evidence record holding two proofs: what the screen showed and what the record held. The integration test case TC-INT-071 found a real defect in the evidence-mismatch advice, which was fixed in Q3.

5. Q3 · August – October 2026

Q3 **Hardening, new screens and production groundwork** · 69 commits · 39 PRs merged

The quarter covered communication material, a forced instance migration, and the largest functional additions since Q1, landed through the first pull-request reviews on main.

Workstream	Deliverable	Status
Stakeholder material	Business overview, technical architecture and plain-English decks, built from scripts and real screenshots	Delivered
ServiceNow fixes	Short description built from available parts; unset state pushed as empty; empty body refused on Update Task and Attest Task	Delivered
Instance migration	Old developer instance reclaimed; app rebuilt from source on dev249570 with deploy scripts 01–10; business-app fields in global scope; suites re-baselined	Delivered
New screens (CAF-233)	Approvals, Reports and Admin screens; grid sort, saved preferences, overdue and selection markers, filters and totals; attestation confirmation; comment limit	Merged · not deployed
Usability (CAF-27)	Clear filters; CSV export with shared helper; callout-log filter; Sync Health filter by record type and stale-check flag; Reports filters	Merged · not deployed
Observability (CAF-218)	Every ServiceNow callout logged through a platform event to `CAF_Integration_Log__c`, surviving rollback	Merged · not deployed
Configuration (CAF-219)	Settings moved from Apex constants into `CAF_Setting__mdt`, read through `CafConfig`	Merged · not deployed
Security (CAF-220)	CRUD and field-level security updates; `CAF_Admin` permission set for the log	Merged · not deployed
Quality (CAF-235, CAF-173)	Apex test suites with mocked callouts (9 test classes); offline LWC unit tests (115 cases) and preflight; mismatch-advice defect fixed	Delivered
Fixes (ad hoc)	Post-decision refresh, review-panel highlight, evidence count relay, empty-filter messages, task-panel reset on request change	Delivered
Architecture pack (October)	Solution HLD PDF with diagrams; technical deck updated to 17 slides	Produced · not committed

Deployment gap. The Salesforce README records the October screen and integration changes as not yet deployed to the Salesforce org. Most Q3 functionality is merged on main but not live. Deploying it is the first Q4 item.

6. Q4 · November 2026 – January 2027 (plan)

Q4 **Production readiness** · forecast

The plan comes from the known limitations recorded in the design document and READMEs. Ordering and scope are proposals for agreement, not commitments.

#	Deliverable	Why	Priority
1	Deploy the Q3 changes to the Salesforce org	Screens, logging, configuration and permission changes are merged but not live	High
2	Apex test class for `CafSyncHealth`	The only Apex class without tests; Salesforce requires 75% coverage to deploy to production	High
3	Execute the pending integration cases	Write-path cases were held back by decision; the harness for them already exists	High
4	Named approver	Audit trail records only `sf.integration`; approval notifications never fire	High
5	Queued delivery with retry	A ServiceNow outage currently fails the user's action	Medium
6	Scheduled Sync Health with alerting	Drift is found only when someone opens the dashboard	Medium
7	JWT bearer for outbound authentication	Client credentials were a recorded deviation; JWT is the production target	Medium
8	Row-level security and Experience Cloud site	Deferred for the proof of concept; needed to realise the licensing benefit	Low

7. Risks, issues and dependencies

Item	Type	Impact and response
Q3 work not deployed	Issue	Stakeholders see August functionality in the org. Response: Q4 item 1.
Developer-instance volatility	Risk	One ServiceNow instance was reclaimed in Q3. Response: the scripted rebuild under `servicenow/deploy` proved the app can be recreated from source.
Echo-loop guard bound to the integration user name	Risk	A wrong inbound user causes a push loop that spends the API budget. Response: preflight checks; monitor the integration log.
Weakest audit link: no named approver	Risk	Compliance evidence chain names the integration account. Response: Q4 item 4.
Rebased commit history	Issue	Several October commits duplicate earlier ones with new dates, which complicates reporting. Response: counts in this report are by author date; duplicates are noted below.
Salesforce API budget (15,000 per day)	Dependency	Shared by integration traffic, deploys and test runs; one end-to-end journey costs about 45 calls.

Method and data notes

- Source: `git log` on main at 571386c. Commit counts exclude merge commits and use author dates.
- Ticketed work (CAF-27, CAF-233 and ad hoc fixes) carries author dates as early as May but reached main through pull requests merged in October. It is reported in Q3, when it landed.
- About 25 October commits repeat earlier subjects after a rebase. By unique subject, Q3 has 44 distinct changes rather than 69.
- Author names were grouped as three people on the assumption that variants are the same person: Geethasri Chintha / Geethasshri; Rehan Sadiq / sadiqrehann / Sadiq Rehan Mohammed; Faiza Aslam. "Reyantech" is an organisation account.
- Q4 is a forecast built from the documented limitations, not from scheduled tickets.
