CONTRIBUTION REPORT · INDIVIDUAL

Rehan Sadiq
CAF Compliance

What Rehan delivered on the ServiceNow ⇄ Salesforce CAF integration from May to October 2026, drawn from the git history, GitHub pull requests and Jira.

Contributor	Rehan Sadiq (also commits as "sadiqrehann" and "Sadiq Rehan Mohammed")
Period	20 May – 23 October 2026
Source	caf-sf-integration repository, main @ 125ac13
Date	23 October 2026

1. Summary


Rehan is the project's test engineer. They built the Playwright test harness and its seed data, wrote the integration and ServiceNow test suites and their test-case catalogues, and recorded the case results used as evidence. In August they fixed the harness's JSON parsing. Commits dated August and September carry their ad hoc testing of the Approvals screen, Jest tests for the Lightning screens and a `.env` preflight check. The history places those commits in October (see "Dating" in section 4). In October they added the Apex test suites with mocked callouts (CAF-235). Later in October they moved into Salesforce build work and delivered six tickets of the October epic. CAF-218: fixed the blockers that stopped the callout log deploying. CAF-221: the CAF Viewer, Owner and Approver permission sets, with a role check on every action that writes to ServiceNow. CAF-222/226: the CAF Compliance Lightning app, tabs, icons and list views. CAF-224: the cafHome page with KPI tiles. CAF-229 and CAF-230: the task and request record pages. In Jira they own 55 CAF work items, mostly in the ETL and data quality epic. 35 are Done, and 9 of those were closed in October. Appendix A lists every Done ticket.

43
distinct changes on main (50 commits incl. repeats)

25%
of the team's 174 distinct changes

104
files touched

12.8k
lines added, excluding 16.2k of generated package-lock.json

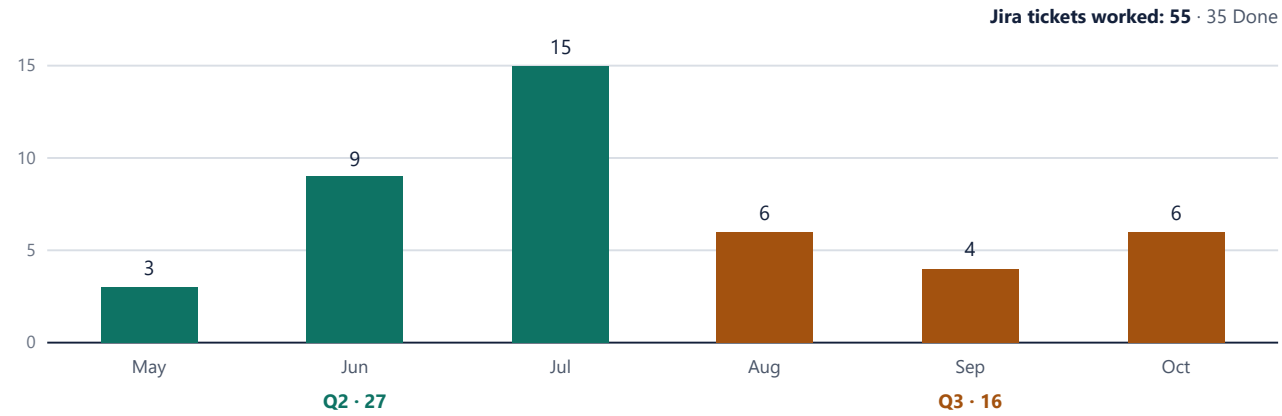

Bars: distinct code changes per month, by the date each commit carries. Repeated copies of a change are counted once, under the earlier date. 8 of these changes (4 in August, 4 in September) carry dates the history contradicts: their commits sit on top of commits made in October, so they cannot have been made in the month shown. Dated by what the history supports, all 8 belong in October (see "Dating" in section 4). Rehan made no commits in Q1 (February–April). Jira tickets worked: CAF work items assigned to Rehan at the time of writing (see section 4 and Appendix A). Section 3 shows when the code reached main.

Quarter	Focus	What they delivered
Q2 May–Jul	Integration test harness	Salesforce JSON assertion helpers and a `cnit` CLI wrapper for record queries; seed data for the demo estate, volume testing, connectivity probes and repairing CAF record numbering; outbound ETL, ServiceNow case, spike and Lightning probe suites; integration and ServiceNow test-case catalogues; recorded case results; README data hazards and RUN-TESTS troubleshooting

Quarter	Focus	What they delivered
Q3 Aug–Oct	Unit testing; Salesforce build	August: harness JSON-parsing fixes. Dated August–September, placed in October by the history: ad hoc testing of the Approvals screen in five rounds (unit tests TC-UNIT-109 to 117, filters, review panel, refresh); offline Jest tests for the Lightning screens and a `.env` preflight check. October: CAF-235 Apex test suites with mocked callouts; CAF-218 deploy fixes; CAF-221 permission sets and role checks; CAF-222/226 Lightning app, tabs and list views; CAF-224 cafHome; CAF-229 and CAF-230 record pages

2. Work by area

Area	Lines added	Main items
Test results (evidence)	2,904	16 recorded case results for the integration (TC-INT) and ServiceNow (TC-SN) suites
Test documentation	2,187	Integration, ServiceNow and unit test-case catalogues; testing README; RUN-TESTS guide
Lightning unit tests (Jest)	1,806	Tests for cafApprovals, cafDashboard, cafEvidence, cafHome, cafTaskHeader and cafTaskTimeline
Playwright specs	1,481	Integration ETL, read-only, UI and negative suites; ServiceNow cases; spike harness; Lightning probe
App shell, home and record pages	1,375	CAF Compliance Lightning app, tabs and list views; cafHome with CafHomeController; cafTaskHeader and the task record page; cafTaskTimeline and the request record page
Apex tests	964	Tests for task, evidence, attestation, dashboard, callout, config and home classes, plus CafTestSupport; CafAccessTest for the role checks; CAF-218 test fixes
Seed data	858	Demo estate, background seeding, generic business apps, connectivity probe, numbering repair
Harness library and preflight	825	`cnit` wrapper, `parseSfJson` helpers, `.env` preflight check and its tests
Permissions and access control	296	CAF Viewer, Owner and Approver permission sets; CAF_Work_Tasks and CAF_Attest custom permissions; CafAccess checks in the task, evidence and attestation services; log trigger fix
Project configuration	122	Jest config, package.json and sfdx-project.json; package.xml entries

Line counts are lines added on main, excluding merges. A generated `salesforce/package-lock.json` (16,180 lines over two commits) is left out. Recorded results are JSON evidence files, so they count high. Repeated copies of a change are counted each time, as in earlier versions of this report. The cafHome change is on main twice (553 lines each), and the five ad hoc rounds and the Jest/preflight commit are also on main twice.

Ticket and test-case references in commits

Reference	Changes	Scope
CAF-235	1	Apex test suites with mocked callouts
CAF-218	1	Deploy blockers: cafCsv missing from package.xml, a formula field set in a test, log writes moved to system mode
CAF-221	1	CAF Viewer, Owner and Approver permission sets; actions checked by custom permission
CAF-222/226	1	CAF Compliance app, Controls tab, tab icons, Overdue and Awaiting attestation list views

Reference	Changes	Scope
CAF-224	1	cafHome with KPI tiles (on main twice; see section 4, "Dating")
CAF-229	1	Task record page with cafTaskHeader, cafEvidence and cafAttestation
CAF-230	1	Request record page with cafTaskTimeline
Ad hoc (approvals)	5	Unit tests TC-UNIT-109 to 117; support dropdown and empty-filter message; review panel highlight, close and evidence count; post-decision and failed refresh
Test cases	6	TC-INT-020, TC-INT-035, TC-INT-037, TC-INT-065, TC-INT-070, TC-SN-017

Ad hoc testing

Alongside the planned suites, Rehan ran ad hoc testing of the Approvals screen. Each round added Jest unit tests to `cafApprovals.test.js` and entries to the unit test-case catalogue. The history places all five rounds on the `adhoc-test` branch in October, and they were merged to main the same month. Each round is also on main as a second copy dated in August or September. Those copies were made on top of October commits, so the dates they carry cannot be when they were made. Whether the testing itself was done earlier is not something git can show.

Earliest possible	Date in copy	What was tested	Lines	Pull request
20 Oct	3 Aug	Unit tests TC-UNIT-109 to 113	+107	#31
20 Oct	9 Aug	Unit tests TC-UNIT-114 to 117	+88	#33
19 Oct	20 Aug	Support dropdown and empty-filter message	+38	#25
20 Oct	28 Aug	Review panel highlight, close and evidence count relay	+80	#27
20 Oct	3 Sep	Post-decision refresh and failed refresh	+56	#29

369 lines in all. The ad hoc work has no Jira tickets, so it does not appear in section 4 or Appendix A. Logging future ad hoc rounds in Jira would make this work visible there.

3. Pull requests

All 47 pull requests were opened and merged through the Reyantech organisation account in October, so GitHub's author field does not show who did the work. The table below attributes each pull request by the authors of the commits it contains. Most of Rehan's work, the May–August harness and suites, went to main directly: only 21 of their 50 commits are in a pull request.

21
of 47 pull requests contain their commits

13
of 31 code-carrying pull requests are entirely theirs

3.7k
hand-written lines added in those 13 (11.8k incl. package-lock)

0
reviews or comments recorded on any pull request

Branch	Pull requests	Lines +/−	Content
test/CAF-235-apex-test-suites	#4 (+#7, #9 sync)	+724 / −0	Apex test suites with mocked callouts
test/lwc-unit-tests-and-preflight	#10 (+#11 sync)	+8,832 / −0	Offline Jest tests and `.env` preflight; 8,090 lines are package-lock.json
adhoc-test	#25, #27, #29, #31, #33 (+4 sync)	+369 / −0	Approvals screen unit tests and ad hoc cases
servicenow-redeploy-dev249570	#8 (shared, sync)	—	2 of 3 commits, no line changes
feature/CAF-217-foundation-pages	#42 – #47	+1,862 / −19	CAF-218 deploy fixes; CAF-221 permission sets and role check; CAF-222/226 Lightning app, tabs and list views; CAF-224 cafHome; CAF-229 task record page; CAF-230 request record page

"Sync" pull requests contain their commits but change no lines; they bring a branch back in line with main. #45 carries the cafHome change twice: once dated October and once dated September (see section 4, "Dating").

4. Jira

In Jira (reyantech.atlassian.net) Rehan appears as "Sadiq Rehan Mohammed". They are the assignee on 56 CAF issues: the ETL and data quality epic (CAF-31) and 55 work items, mostly integration test cases (TC-INT), with stories, bugs, tasks and subtasks.

55
CAF work items assigned (excluding epics)

35
Done (64%)

9
closed in October

16
To Do (6 in the October 2026 epic), plus 2 In Progress and 2 In Review

Epic	Title	Done / items	Epic status
CAF-31	ETL and data quality assurance	26 / 35	Done
CAF-32	Defect remediation and open items	5 / 8	Done
CAF-12	CAF business logic and server scripts	1 / 1	To Do
CAF-217	October 2026: foundation, app shell, home and record pages	3 / 11	In Progress

CAF-31 holds 30 test cases and 5 stories. CAF-32 counts two subtasks: CAF-244 under CAF-79 and CAF-246 under CAF-180. CAF-12 counts one subtask (CAF-18) under CAF-13. CAF-217 counts one subtask, CAF-248, under CAF-233. CAF-31 is the only epic assigned to Rehan; the status of the others is shown for context.

Changes since the previous version of this report

- **Now Done:** CAF-106 (TC-INT-005 idempotent push) and CAF-142 (TC-INT-041 drift type 2), both closed in October.
- **Now In Review:** CAF-110 (TC-INT-009 push failures do not roll back) and CAF-111 (TC-INT-010 kill switch), previously To Do.
- **Now In Progress:** CAF-238 (retest cycle C2), previously To Do.
- **New:** CAF-248, a subtask under CAF-233 to validate the control catalogue instructions and request tier mapping, In Progress.
- **Code:** pull requests #42 – #47 merged to main: CAF-218, CAF-221, CAF-222/226, CAF-224, CAF-229 and CAF-230. Together they add 7 commits (6 distinct changes) and 2,415 lines. No Jira ticket changed with them.
- **Dating:** eight changes carry August or September dates that the history contradicts. The monthly chart shows them in the month they carry, and its caption says so (see "Dating" below).

Earlier changes this month

- **CAF-235** (Apex test suites) was reassigned to Rehan and closed as Done, matching the merged pull request #4.
- **Now Done:** CAF-144 (TC-INT-043 drift type 4), CAF-174 (mirrored Name field never compared), CAF-234 (compliance roll-up fix, newly assigned to Rehan), CAF-239 (retest cycle C3), CAF-244 (Apex service

coverage and negative scenarios) and CAF-246, a new subtask under CAF-180 for ETL testing of credential rotation.

- **Now In Progress:** CAF-106 (TC-INT-005 idempotent push) and CAF-142 (TC-INT-041 drift type 2).

Where Jira and the code disagree

- **Epic Done with open items.** CAF-31 is Done, but 9 of its test cases are still open: 7 To Do and 2 In Review. They include drift types 1 and 3 (TC-INT-039, 042), re-sync repair (TC-INT-040) and the kill switch (TC-INT-010, In Review).
- **Code merged, ticket still open.** CAF-240 ("Jest set-up and unit tests for the existing LWCs") is To Do, although Rehan's Jest tests were merged in pull request #10 in October.
- **Code merged, ticket with someone else.** Seven tickets are assigned to Geethasri Chintha and marked To Do although Rehan's commits for them were merged in October: CAF-218 (#42), CAF-221 (#43), CAF-222 and CAF-226 (#44), CAF-224 (#45), CAF-229 (#46) and CAF-230 (#47). CAF-218 was Geethasri's build, and Rehan's commit fixed its deploy blockers. The other six are Rehan's work throughout.
- **Matches.** For the harness and suites, dates line up: tickets were created May–July, the same months as the commits. Test cases named in commits match Done tickets, for example TC-INT-065 (CAF-166) and TC-INT-070 (CAF-171), and recorded results TC-INT-063 and 064 (CAF-164, CAF-165).

Dating

A commit cannot be made before the commits it is built on. Eight of Rehan's commits on main are dated earlier than commits they are built on, so the dates they carry cannot be when they were made. Seven are second copies of a change that is also on main with an October date. In every pair, the two copies have the same minutes and seconds and differ only in day and hour. For example, the cafHome change (CAF-224) is on main as 8e6b369, dated October, and as dac5fd0, dated September. dac5fd0 sits on top of a commit made in October.

Copy and date it carries	Built on a commit from	Change
f7e3a17 · 3 Aug	20 Oct	Ad hoc: TC-UNIT-109 to 113
8aaae1d · 9 Aug	20 Oct	Ad hoc: TC-UNIT-114 to 117
089cf3e · 20 Aug	19 Oct	Ad hoc: support dropdown and empty-filter message
d09cb51 · 28 Aug	20 Oct	Ad hoc: review panel highlight, close and evidence count relay
a899c85 · 3 Sep	20 Oct	Ad hoc: post-decision refresh and failed refresh
893236d · 10 Sep	17 Oct	Offline LWC unit tests and `.env` preflight check
08b1e7b · 17 Sep	16 Oct	Merge of the CAF-235 Apex test branch (a single-parent commit)
dac5fd0 · 25 Sep	23 Oct	CAF-224: cafHome with KPI tiles

The monthly chart in section 1 shows each change in the month it carries, and its caption counts the eight above. The earliest date the history supports is the commit's own date or the latest date of anything it is built on, whichever is later. By that rule, 4 of the August changes and all 4 September changes belong in October,

which would make the months August 2, September 0 and October 14. Git shows when a commit was made, not when the work behind it was done. The same pattern appears in other contributors' commits on main.

Method and caveats

- Source: `git log main --no-merges` at 125ac13, filtered by the email rehan.sadiq@reyantech.co.uk, which covers all three author names. The figures at the previous source were reproduced exactly before updating.
- 7 of their 50 commits repeat the subject of another. Counts of "changes" use distinct subjects, dated by the earlier copy, with contradicted dates noted as described under "Dating". The Geethasri Chintha report uses the same method.
- Commits measure activity, not effort or quality. Manual test execution, review and pairing are not captured.
- Pull request data: `gh pr view` for #1–#41, read in October 2026, and #42–#47, read later in October. A pull request counts as theirs when every commit in it carries their email.
- Jira data: issues assigned to account "Sadiq Rehan Mohammed", read in October 2026.

Appendix A. Done Jira tickets

Every CAF work item assigned to Rehan in Jira with status Done at the time of writing, 35 in total, grouped by epic. A ticket is listed whether or not a commit names it. Tickets marked **Oct** were closed in October.

CAF-31 ETL and data quality assurance (26)

Ticket	Type	Summary
CAF-97	Story	Seed a demo estate that reads to an audience who does not know the client
CAF-98	Story	Seed through a server-side script rather than the Table API
CAF-99	Story	Reconcile the number counter before any bulk insert
CAF-100	Story	Key duplicate-request detection on the control, not the relationship
CAF-101	Story	Take the detached requests out of both grids
CAF-102	Test	TC-INT-001 Full mirror parity by record, not by count
CAF-105	Test	TC-INT-004 Tasks created by the flow are pushed too
CAF-106	Test	TC-INT-005 Push is idempotent Oct
CAF-107	Test	TC-INT-006 No Salesforce Id is ever stored in ServiceNow
CAF-109	Test	TC-INT-008 Blank and null are treated as equal
CAF-139	Test	TC-INT-038 Clean state reports zero differences
CAF-142	Test	TC-INT-041 Drift type 2: in ServiceNow, missing in Salesforce Oct
CAF-144	Test	TC-INT-043 Drift type 4: Salesforce simply stale Oct
CAF-145	Test	TC-INT-044 Only State__c is editable in the Salesforce mirror
CAF-147	Test	TC-INT-046 Snapshot is read-only
CAF-148	Test	TC-INT-047 Drift detection is automatic, repair never is
CAF-159	Test	TC-INT-058 Updating a pending-delete record recreates its twin
CAF-163	Test	TC-INT-062 The control catalogue is reconciled by nothing
CAF-164	Test	TC-INT-063 The External Id is unique and always populated
CAF-165	Test	TC-INT-064 Truncation headroom, and the drift it would cause
CAF-166	Test	TC-INT-065 Date conversion fidelity
CAF-167	Test	TC-INT-066 The state code-to-label mapping is total
CAF-168	Test	TC-INT-067 Denormalised business application is still current
CAF-169	Test	TC-INT-068 The control join resolves, and the name agrees
CAF-170	Test	TC-INT-069 The boolean cast survives the round trip
CAF-171	Test	TC-INT-070 Parent references resolve

CAF-32 Defect remediation and open items (5)

Ticket	Type	Summary
CAF-174	Bug	Name is a mirrored field that is editable and never compared Oct
CAF-176	Bug	A deleted control left an active orphan column in the dashboard
CAF-178	Bug	Control numbers are not unique, so any join keyed on them pairs the wrong records
CAF-244	Subtask	Validate Apex Service Test Coverage and Negative Scenarios Oct
CAF-246	Subtask	ETL Testing – Validate Credential Rotation and Salesforce–ServiceNow Integration Oct

CAF-217 October 2026: foundation, app shell, home and record pages (3)

Ticket	Type	Summary
CAF-234	Bug	ServiceNow: fix the compliance roll-up business rule (DEF-01, DEF-02) Oct
CAF-235	Story	Apex test suites with mocked callouts Oct
CAF-239	Task	Retest cycle C3: verify the 12 August fixes (RT-17, RT-18) Oct

CAF-12 CAF business logic and server scripts (via CAF-13) (1)

Ticket	Type	Summary
CAF-18	Subtask	Test next due date calculation on request closure
