CONTRIBUTION REPORT · INDIVIDUAL

Geethasri Chintha CAF Compliance

What Geethasri has delivered on the ServiceNow ⇄ Salesforce CAF integration from April 2026, and the work assigned to them through to project closure in March 2027, drawn from the git history, GitHub pull requests and Jira.

Contributor	Geethasri Chintha (also commits as "Geethasshri")
Period	April 2026 – March 2027
Recorded to date	April – 24 October 2026
Planned	November 2026 – March 2027
Source	caf-sf-integration repository, main @ 9a52d51
Date	24 October 2026

1. Summary


Geethasri is the largest single contributor to the repository. Commits dated April carry the first four Lightning screens (Dashboard, Evidence, Attestation, Sync Health) and the ServiceNow outbound sync. Commits dated May carry the push and retire business rules and the six ServiceNow REST endpoints, followed by the setup guide and design decisions in June and July, and the presentation decks and ServiceNow fixes in August. These commits, dated April to 12 August, reached the repository in a single merge on 12 August 2026. Commits dated May to October also carry the ticketed UI work on the Approvals, Reports, Admin and Sync Health screens (CAF-27, CAF-233) and the task-panel and evidence fixes, which the history places in October (see "Dating" in section 4). In October they also delivered the hardening tickets (CAF-173, CAF-218, CAF-219, CAF-220), which were deployed to the Salesforce org on 21 October. Their commits appear in 27 of the 47 pull requests, all merged in October. In Jira they own 81 CAF work items, 61 Done. Section 5 lists the work assigned to them for November 2026 to March 2027.

57
distinct changes dated April – October

27
of 47 pull requests contain their commits

61
of 81 CAF Jira work items Done

9
Jira items open for November – March

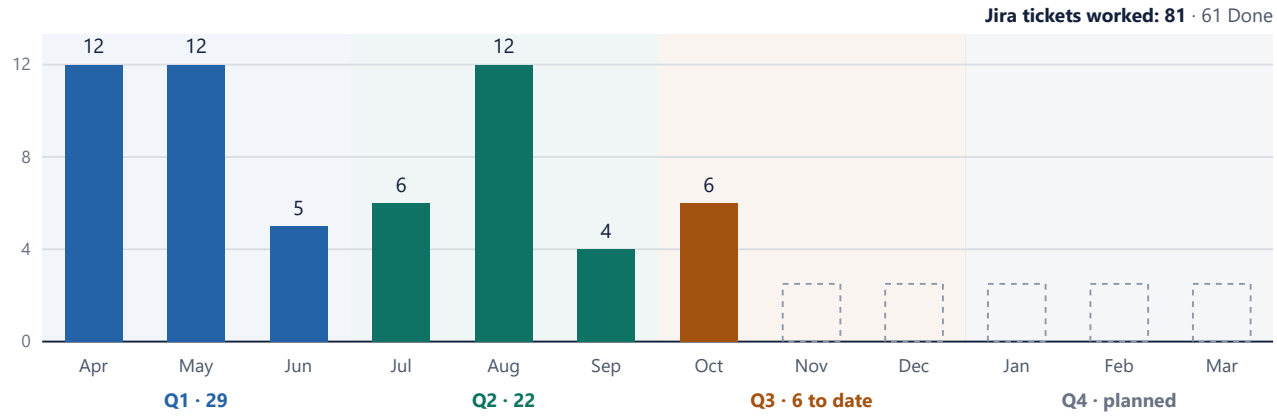

Bars: distinct code changes per month, by the date each commit carries. Repeated copies of a change are counted once, under the earlier date. Commits dated April to 12 August reached the repository in one merge on 12 August 2026. 16 of these changes (May 2, June 3, July 5, August 1, September 4, October 1) carry dates the history contradicts: their commits sit on top of commits made in October, so they cannot have been made in the month shown. Dated by what the history supports, all 16 belong in October (see "Dating" in section 4). Outlines from November are planned months, not a forecast of volume. Jira tickets worked: CAF work items assigned to Geethasri at the time of writing (see section 4 and Appendix A).

Quarter	Focus	What they delivered
Q1 Apr–Jun 2026	Lightning screens, ServiceNow sync and API	Dated April: Dashboard, Evidence, Attestation and Sync Health screens; CAFSalesforceSync, caf_short_desc and the control push rule. Dated May: request push and control retire rules; six scripted REST endpoints; ServiceNow setup guide. Dated June: verified behaviour; key design decisions. Dated May–June, placed in October by the history: CAF-27 clear filters, CSV export and callout-log changes

Quarter	Focus	What they delivered
Q2 Jul–Sep 2026	Decks and ServiceNow fixes	Dated July: known gaps in the setup guide. Dated August: business and technical deck builders and screenshots; ServiceNow short-description and null-state fixes. Dated July–September, placed in October by the history: CAF-27 Sync Health and Reports changes; CAF-233 Approvals screen, null checks, grid sort and saved preferences; approvals test validations; task-panel, evidence-reload and outage-reporting fixes
Q3 Oct–Dec 2026	Hardening; workflow and UAT planned	October: CAF-233 grid filters and totals; CAF-173, CAF-218, CAF-219, CAF-220, merged and deployed to the Salesforce org on 21 October. November–December: planned items in section 5
Q4 Jan–Mar 2027	Planned	Project milestones: defect resolution, production readiness and handover. No Jira items assigned to them yet (section 5)

2. Work by area

Area	Lines added	Main items
Salesforce · Lightning (LWC)	12,667	cafDashboard, cafEvidence, cafAttestation, cafSyncHealth; Approvals, Reports and Admin screen changes; shared cafCsv helper
Salesforce · Apex	2,645	CafTaskService, CafEvidenceService, CafAttestationService, CafDashboardController, CafSyncHealth; callout logging; custom-metadata settings
Salesforce · metadata	1,506	Control Catalog, Request and Task objects; permission set; layouts, tabs, manifest, custom metadata, triggers
ServiceNow	1,427	CAFSalesforceSync script include, caf_short_desc helper, business rules, six REST endpoints, SETUP.md
Design and docs	1,541	Technical design document (diagram, security model, key design decisions), README, deployment notes, handoff archive
Presentation	1,644	Business overview and technical architecture deck builders, screenshot cropping utility, captured screenshots
Testing	990	Approvals test validations

Line counts are lines added on main, excluding merges, across all of their commits including the 19 dated February and March 2026. Generated or bulk files (for example LWC markup and deck images) push some areas up.

Ticketed work

Ticket	Changes	Scope
CAF-27	8	Clear-filters button; CSV export; callout log filter by operation and clearer empty states; Sync Health record-type filter and stale-check flag (15 min); Reports overdue-only and click-to-filter
CAF-233	4	Approvals screen redesign; null checks and method comments; grid sort, saved preferences, overdue and selection markers, task summary, sync breakdown, comment limit; grid filters and totals, attestation confirmation
CAF-173	1	Mismatch advice names the side that is short
CAF-218	1	Log every ServiceNow callout
CAF-219	1	Move CAF settings from Apex constants into custom metadata
CAF-220	1	CRUD updates

3. Pull requests

All 47 pull requests were opened and merged through the Reyantech organisation account in October, so GitHub's author field does not show who did the work. The table below attributes each pull request by the authors of the commits it contains. The six most recent (#42–#47) carry only Rehan Sadiq's commits.

27
of 47 pull requests contain their commits

17
of 31 code-carrying pull requests are entirely theirs

7.1k
lines added in those 17 (350 removed)

0
reviews or comments recorded on any pull request

Branch	Pull requests	Lines +/−	Content
feature/CAF-218-integration-log	#2	+396 / −33	Log every ServiceNow callout
feature/CAF-220-crud-fls	#3	+30 / −0	CRUD updates
fix/CAF-173-mismatch-advice	#5	+15 / −5	Mismatch advice names the short side
feature/CAF-118-enhance-fix	#12 (#13 sync)	+254 / −34	Task panel, evidence reload and outage-reporting fixes
feature/CAF-233-push-controls	#14, #16, #18, #21, #23 (+6 sync)	+5,651 / −250	Approvals screen, test validations, null checks, grid sort, filters and totals
CAF-27-sync-health-drift	#34 – #41	+770 / −28	Filters, CSV export, callout log, Sync Health and Reports changes
feature/CAF-219-config-custom-metadata	#1 (shared)	—	1 of 9 commits: settings moved to custom metadata

"Sync" pull requests contain their commits but change no lines; they bring a branch back in line with main. Pull requests #6 and #7 (ServiceNow redeploy and Apex test branches) are of this kind. Lines for CAF-27 are summed across the eight pull requests on that branch.

4. Jira

In Jira (reyantech.atlassian.net) Geethasri appears as "Chintha Geetha sri". They are the assignee on 93 issues in the CAF project: 12 epics and 81 work items (stories, bugs, tests, tasks and subtasks). Another 26 issues assigned to them sit in other projects (MONO, SCRUM, HP) from January 2025 and are left out here.

81
CAF work items assigned (excluding epics)

61
Done (75%)

4
closed in October

17
To Do (15 in the October 2026 epic), plus 3 in progress, testing or review

Epic	Title	Done / items	Epic status
CAF-23	Salesforce foundation and org setup	8 / 8	Done
CAF-24	Outbound integration – ServiceNow to Salesforce	9 / 9	Done
CAF-25	Inbound integration – Salesforce to ServiceNow	6 / 6	Done
CAF-26	CAF compliance dashboard (LWC)	6 / 6	Done
CAF-27	Sync Health and drift detection	7 / 7	Done
CAF-28	Evidence and attestation	7 / 7	Done
CAF-3	CAF data model and tables (ServiceNow)	6 / 8	To Do
CAF-12	CAF business logic and server scripts	5 / 5	To Do
CAF-31	ETL and data quality assurance	2 / 2	—
CAF-32	Defect remediation and open items	5 / 7	Done
CAF-217	October 2026: foundation, app shell, home and record pages	0 / 16	In Progress

Counts include subtasks (three under CAF-3, one under CAF-12). CAF-31 is not assigned to Geethasri, so its status is not shown. Two more epics assigned to them, CAF-189 ("login page error", To Do) and CAF-190 (an earlier copy of the October epic, In Progress), have no work items assigned to them.

Changes since the previous version of this report

- **Period:** now April 2026 – March 2027. The 19 changes dated February and March 2026 are left out of the chart, the quarter table and the change count; the area table and Appendix A still cover all of their work. Section 5 adds the work assigned for November – March.
- **Now Done:** CAF-104 (TC-INT-003, a new task appears in Salesforce) and CAF-181 (the evidence gate binds the API but not the portal or an administrator).
- **Moved forward:** CAF-233 from In Progress to Testing.
- **Code:** no new commits of theirs. Six more pull requests merged in October (#42–#47), all Rehan Sadiq's, so the team totals moved: 174 distinct changes (was 168) and 47 pull requests (was 41).

- **Dating:** sixteen changes carry May–October dates that the history contradicts. The monthly chart shows them in the month they carry, and its caption says so (see "Dating" below).

Earlier changes this month

- **Now Done:** CAF-180 (integration credentials exposed in a session transcript) and CAF-79 (Apex test coverage for the three service classes).
- **Moved forward:** CAF-233 from To Do to In Progress; CAF-181 from In Progress to Testing.
- **Moved back:** CAF-218, CAF-219 and CAF-220 from In Review to To Do.
- **Reassigned:** CAF-234 (compliance roll-up fix) moved to Rehan Sadiq, who closed it in October.

Where Jira and the code disagree

- **Code merged, ticket still open.** CAF-233 is in Testing although its code was merged through pull requests #14–#24 in October. CAF-218, CAF-219 and CAF-220 were moved back from In Review to To Do, although their code is merged.
- **Assigned to Geethasri, built by someone else.** CAF-221, CAF-222, CAF-224, CAF-226, CAF-229 and CAF-230 are assigned to Geethasri and To Do, but Rehan Sadiq's commits for all six were merged in October (#43–#47). Rehan also merged a deploy fix for CAF-218 (#42).
- **Done epics with open items.** CAF-32 (defect remediation) is Done with two of its seven items still open: CAF-185 and CAF-78. CAF-3 and CAF-12 are the opposite: all their stories are done but the epics are still To Do.
- **Assignee differs from author.** CAF-173 and CAF-118 are assigned to Faiza Aslam, but the commits that fix them (#5, #12) are Geethasri's.
- **Dates do not line up.** Many CAF issues were created between August 2025 and January 2026, before the repository's first commit in February 2026. Most Done issues also have no resolution date. So Jira cannot be used to measure how long the work took.

Dating

A commit cannot be made before the commits it is built on. Sixteen of Geethasri's commits on main are dated earlier than commits they are built on, so the dates they carry cannot be when they were made. Each is a second copy of a change that is also on main with an October date. In all sixteen pairs the two copies have the same minutes and seconds and differ only in day and hour. For example, "CAF-27: Clear filters button" is on main as 868a7a9, dated October, and as 7ed82f6, dated May. 7ed82f6 sits on top of a commit made in October.

Copy and date it carries	Built on a commit from	Change
7ed82f6 · 20 May	20 Oct	CAF-27: Clear filters button
84026e7 · 26 May	20 Oct	CAF-27: Export CSV, shared cafCsv helper
63e7578 · 3 Jun	20 Oct	CAF-27: Admin - filter callout log by operation
33b1bd8 · 8 Jun	20 Oct	CAF-27: Admin - clearer empty callout log messages
7c8ffd3 · 30 Jun	20 Oct	CAF-27: Sync Health - filter differences by record type
31d5546 · 3 Jul	20 Oct	CAF-27: Sync Health - flag checks older than 15 minutes

Copy and date it carries	Built on a commit from	Change
dde14d5 · 8 Jul	20 Oct	CAF-27: Reports - Overdue only on due dates
2a10717 · 10 Jul	18 Oct	CAF-233: Updated screen for approvals
33488e3 · 10 Jul	20 Oct	CAF-27: Reports - click an application to filter
95c4243 · 19 Jul	19 Oct	CAF-233: Null checks and method comments on Approvals, Reports and Admin screens
99a7f57 · 18 Aug	19 Oct	Updated test validations for approvals
b38edf4 · 1 Sep	18 Oct	Close task panel on request change; fix row highlight; hide actions without sys_id
4f6d179 · 15 Sep	18 Oct	Report unreadable ServiceNow evidence replies separately from outages
502fbaf · 15 Sep	18 Oct	Reload evidence and reset attestation when the task changes
685298f · 25 Sep	19 Oct	CAF-233: Grid sort, saved preferences, overdue and selection markers, task summary
9e91962 · 2 Oct	19 Oct	CAF-233: Grid filters and totals, Sync Health fixes, evidence reload, attestation confirmation

The monthly chart in section 1 shows each change in the month it carries, and its caption counts the sixteen above. The earliest date the history supports is the commit's own date or the latest date of anything it is built on, whichever is later. By that rule, 2 changes move out of May, 3 out of June, 5 out of July, 1 out of August and all 4 out of September into October. The months would then read May 10, June 2, July 1, August 11, September 0 and October 21. Git shows when a commit was made, not when the work behind it was done. The same pattern appears in other contributors' commits on main.

5. Planned work, November 2026 – March 2027

Work assigned to Geethasri in Jira and not yet done, at the time of writing. This is planned work, not delivered work. Jira states are as read in October 2026.

Ticket	Title	Depends on	Month
CAF-218, 219, 220	Close out: code merged and deployed 21 October; tickets moved back to To Do	Review and test	Nov
CAF-232	ServiceNow: push request and task assignee, manager and Business Owner	—	Nov
CAF-223	Utility bar: my open tasks count and sync status chip	CAF-232	Nov
CAF-225	cafMyWork: my open, due in seven days, overdue, recently attested	CAF-232	Nov
CAF-231	Route CafSyncHealth through CafCallout and decide its permission checks	—	Nov
CAF-227	Dashboard v2: filters and search by control, status, tier and my applications	CAF-232, tier push	Dec
CAF-228	Dashboard v2: tooltips, column drill, legend, show/hide, sticky header, CSV export and print	Control instructions push	Dec

CAF-221, CAF-222, CAF-224, CAF-226, CAF-229 and CAF-230 are also assigned to Geethasri in Jira, but they were built and merged under other commits in October (see "Where Jira and the code disagree"), so they are not listed as their planned work. The project's January – March 2027 milestones (defect resolution and regression; production readiness and integration hardening; final validation, UAT sign-off and handover) have no Jira items assigned to Geethasri yet.

Method and caveats

- Source: `git log main --no-merges` at 9a52d51 (24 October 2026), filtered by the email geethasri.chintha@reyantech.co.uk, which covers both author names. No commits of theirs were added between 125ac13 and 9a52d51.
- The repository was created on GitHub on 9 August 2026. Commits dated before then arrived in merge `b4a6eea` on 12 August 2026 and carry the dates recorded by their authors.
- 16 of their 92 commits repeat the subject of another. Counts of "changes" use distinct subjects, dated by the earlier copy, with contradicted dates noted as described under "Dating". Line counts include every copy, as in earlier versions of this report.
- Commits measure activity, not effort or quality. Review, pairing and testing in the org are not captured.
- Jira data: issues assigned to account "Chintha Geetha sri", read in October 2026.
- Pull request data: `gh pr view` for #1–#41, read in October 2026, and #42–#47, read later in October. A pull request counts as theirs when every commit in it carries their email.

Appendix A. Done Jira tickets

Every CAF work item assigned to Geethasri in Jira with status Done at the time of writing, 61 in total, grouped by epic. A ticket is listed whether or not a commit names it. Jira issue keys are not used in most commit messages, so most of these tickets cannot be matched to a specific commit. Tickets marked **Oct** were closed in October.

CAF-3 CAF Data Model & Tables (6)

Ticket	Type	Summary
CAF-2	Story	Create CAF Controls table (caf_conformance_type)
CAF-4	Story	Create CAF Controls Relationships table (caf_relationship)
CAF-5	Subtask	Verify table schema and field attributes across all five tables
CAF-6	Story	Create CAF Relationship Tasks template table
CAF-7	Story	Create CAF Request table (caf_req)
CAF-8	Story	Create CAF Task table (caf_tsk)

CAF-12 CAF Business Logic & Server Scripts (5)

Ticket	Type	Summary
CAF-13	Story	BR: Manage active flag on request close/cancel
CAF-14	Story	BR: Set actual end date and calculate next due date on request close
CAF-15	Story	BR: Update Business App compliance status on out_of_compliance
CAF-16	Story	BR: Set Business App to undergoing_update on request insert
CAF-20	Subtask	Test CAFUtil.generateCAFRequests creates one request per matching relationship

CAF-23 Salesforce foundation and org setup (8)

Ticket	Type	Summary
CAF-33	Story	Provision the Salesforce Developer Edition org and record its platform limits
CAF-34	Story	Establish the metadata-format source tree and a repeatable deploy
CAF-35	Story	Create CAF_Request__c with ServiceNow_Sys_Id__c as the External Id
CAF-36	Story	Create CAF_Task__c parented to CAF_Request__c
CAF-37	Story	Grant field-level security through the CAF_Integration permission set
CAF-38	Story	Add the custom fields to the page layouts
CAF-39	Story	Define All list views with explicit columns
CAF-40	Story	Create the tabs for the dashboard and the CAF objects

CAF-24 Outbound integration - ServiceNow to Salesforce (9)

Ticket	Type	Summary
CAF-41	Story	Authenticate ServiceNow to Salesforce with the Client Credentials flow
CAF-42	Story	Hold the Salesforce credentials as ServiceNow system properties
CAF-43	Story	Build CAFSalesforceSync - token, transform and upsert by External Id
CAF-44	Story	Push a CAF Request to Salesforce on insert and update
CAF-45	Story	Push a CAF Task to Salesforce on insert and update
CAF-46	Story	Transform ServiceNow values into their Salesforce shapes
CAF-47	Story	Add a kill switch that stops all outbound push
CAF-48	Story	Make a failed push fire-and-forget, and log it
CAF-49	Story	Guard against the echo loop without stranding derived changes

CAF-25 Inbound integration - Salesforce to ServiceNow (6)

Ticket	Type	Summary
CAF-50	Story	Create the sf.integration user and settle basic auth on the instance
CAF-51	Story	Build the inbound task update API with a six-field allow-list
CAF-52	Story	Create the ServiceNow_CAF named credential
CAF-53	Story	Build CafTaskService.applyChange
CAF-54	Story	Reconcile derived changes explicitly at the end of an inbound write
CAF-55	Story	Unwrap the Scripted REST response envelope in Apex

CAF-26 CAF compliance dashboard (LWC) (6)

Ticket	Type	Summary
CAF-56	Story	Build the CafDashboardController read model
CAF-57	Story	Build the cafDashboard grid LWC
CAF-58	Story	Mirror the control catalogue into CAF_Control_Catalog__c
CAF-59	Story	Derive dashboard columns from the catalogue, not from the requests present
CAF-60	Story	Join requests to controls on sys_id, and backfill the mirrored records
CAF-61	Story	Drill in from a grid cell to the request's tasks

CAF-27 Sync Health and drift detection (7)

Ticket	Type	Summary
CAF-62	Story	Expose a read-only snapshot endpoint

Ticket	Type	Summary
CAF-63	Story	Expose a resync endpoint that re-pushes a single record
CAF-64	Story	Build CafSyncHealth - compare both platforms and report the differences
CAF-65	Story	Build the cafSyncHealth status strip
CAF-66	Story	Reconcile the control catalogue, keyed on sys_id
CAF-67	Story	Mirror a deleted control as retired rather than leaving an orphan column
CAF-68	Story	Retry a push once on a transport-level failure

CAF-28 Evidence and attestation (7)

Ticket	Type	Summary
CAF-69	Story	Accept evidence uploads into ServiceNow as attachments
CAF-70	Story	Expose what ServiceNow actually holds as evidence
CAF-71	Story	Build CafEvidenceService - Salesforce Files in, both lists out
CAF-72	Story	Build the cafEvidence panel with a read-only mode
CAF-73	Story	Build the attest endpoint - the gate, then the outcome
CAF-74	Story	Build CafAttestationService
CAF-75	Story	Build the cafAttestation form

CAF-31 ETL and data quality assurance (2)

Ticket	Type	Summary
CAF-103	Test	TC-INT-002 A new request appears in Salesforce
CAF-104	Test	TC-INT-003 A new task appears in Salesforce Oct

CAF-32 Defect remediation and open items (5)

Ticket	Type	Summary
CAF-79	Story	Write Apex test coverage for the three service classes Oct
CAF-177	Bug	Changes derived from a Salesforce write never reached Salesforce
CAF-179	Bug	Renaming a control strands the old name on every request already mirrored
CAF-180	Bug	Integration credentials were exposed in a session transcript Oct
CAF-181	Bug	The evidence gate binds the API but not the portal or an administrator Oct
