DELIVERABLES REPORT · QUARTERLY

CAF Compliance 12-Month Deliverables

What the ServiceNow ⇄ Salesforce integration project has produced in each quarter from April 2026, and the monthly milestones planned through to project closure on 31 March 2027.

Reporting window	April 2026 – March 2027
Recorded to date	Q1 Apr–Jun · Q2 Jul–Sep · Q3 October (to 24 Oct)
Planned	October 2026 – March 2027, by month (Q3 and Q4)
Project closure	31 March 2027
Source	caf-sf-integration repository, main @ 9a52d51; Salesforce and ServiceNow developer instances
Date	24 October 2026

1. Executive summary

The project gives application owners and approvers a Salesforce experience for CAF compliance while ServiceNow stays the system of record. The repository now holds a tested two-way integration: a Lightning application with a home page, compliance dashboard, approvals, reports, admin, and request and task record pages; a six-resource ServiceNow API; drift detection; durable callout logging; role-based permission sets; and a three-level test pack. The remaining five months take it through workflow completion, ETL testing and customer UAT to production readiness and handover by 31 March 2027.


201
commits on main, excluding merges (one is a misdated duplicate)

47
pull requests merged (#1–#47), September–October

333
files under version control

6
monthly milestones to closure, October 2026 – March 2027

Quarter	Theme	Headline deliverables
Q1 Apr–Jun 2026	Build and integration API	Four Lightning components; ServiceNow outbound sync; request push and retire rules; six inbound REST resources; Playwright harness; test suites
Q2 Jul–Sep 2026	Test evidence, decks and instance rebuild	139 test cases; Word evidence packs; stakeholder decks; ServiceNow rebuilt from source on dev249570; LWC unit tests
Q3 Oct–Dec 2026	Application build, workflow, ETL testing and UAT	October: new screens, logging, configuration, security, home page, record pages (merged). November: workflow and integration. December: reporting, ETL testing, UAT cycles 1 and 2
Q4 Jan–Mar 2027	Defects, production readiness and handover	Defect resolution and regression; production readiness and integration hardening; final validation, UAT sign-off, handover and closure by 31 March 2027

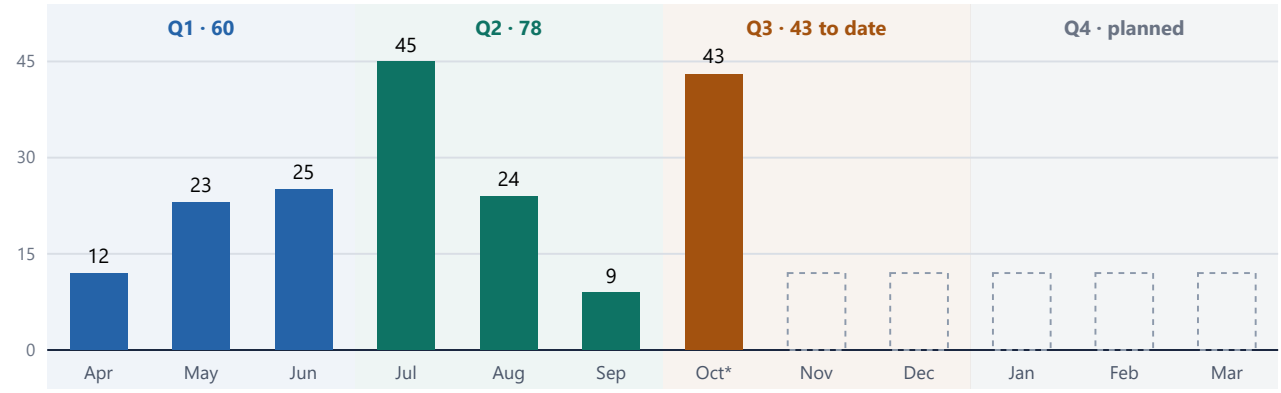

Commits per month on main, excluding merges, by author date. The repository was created on 9 Aug; dates before 12 Aug are unverified. *To 24 Oct.

Figure 1 · Repository activity by month and quarter

2. Milestone timeline

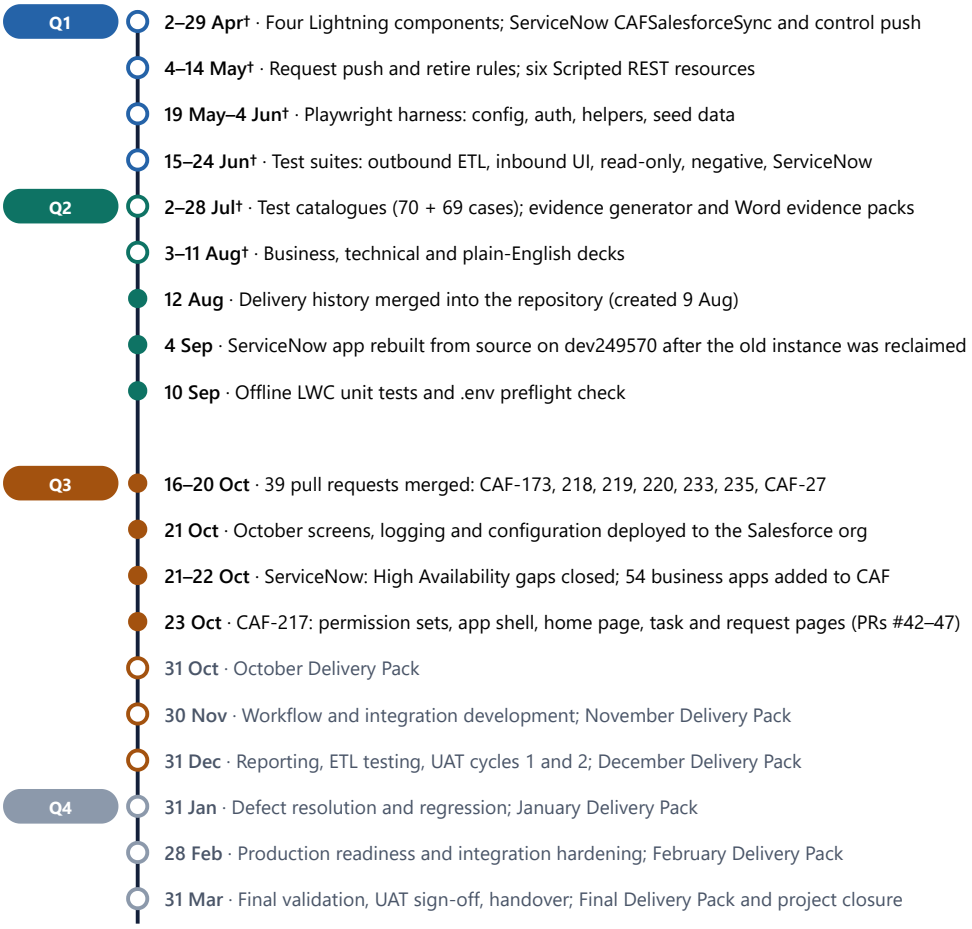


Figure 2 · Key milestones. Filled: recorded. Ringed with †: dated before 12 Aug 2026, unverified. Ringed without †: planned.

3. Q1 · April – June 2026

Q1 **Build and integration API** · 60 commits by author date · all dated before 12 August

The deliverables below are in the repository. Their dates were recorded by their authors before the repository existed on GitHub and cannot be confirmed from the repository itself.

Workstream	Deliverable
Lightning UI	`cafDashboard` compliance grid; `cafEvidence` upload and lists; `cafAttestation` approver flow; `cafSyncHealth` drift panel
ServiceNow outbound	`CAFSalesforceSync` script include; `caf_short_desc` helper; business rules pushing controls and requests and retiring deleted controls
ServiceNow inbound API	Scripted REST resources: sync snapshot, update task, upload evidence, list evidence, attest task, resync record
Configuration guide	ServiceNow setup guide, verified behaviour, inbound contract, known gaps
Test harness	Playwright project with Salesforce and ServiceNow projects; storage-state auth; Lightning page objects; API helpers; watch mode; single-case runner
Test data and suites	Seed definitions, volume seed, connectivity probe; outbound ETL, inbound UI, read-only, negative-path and ServiceNow suites

Outcome

By the end of the quarter, as dated, the integration contract was complete in both directions and the automated harness could exercise it.

4. Q2 · July – September 2026

Q2 **Test evidence, decks and instance rebuild** · 78 commits by author date · 60 dated before 12 Aug, 18 after

Workstream	Deliverable
Test catalogues	70 integration cases and 69 ServiceNow cases, with coverage summaries and run instructions
Evidence	Case-result parser, branded per-case Word evidence packs, HTML evidence report, results for each suite
Stakeholder material	Business overview, technical architecture and plain-English decks, built from scripts and real screenshots
Repository	Delivery history merged into `caf-sf-integration` on GitHub
Instance migration	Old developer instance reclaimed; app rebuilt from source on dev249570 with deploy scripts 01–10; business-app fields in global scope
ServiceNow fixes	Short description built from available parts; unset state pushed as empty; empty body refused on Update Task and Attest Task
Quality	Offline LWC unit tests and `.env` preflight check

Outcome

Every executed case produced a Word evidence record holding two proofs: what the screen showed and what the record held. When the original ServiceNow instance was reclaimed, the scripted rebuild proved the application can be recreated from source.

5. Q3 · October – December 2026

Q3 **Application build, workflow, ETL testing and UAT** · October in progress · November–December planned

Planned work and milestones

Month	Planned work and milestones
October 2026	**CAF Salesforce Application Development.** UX workshops, wireframes and development of the CAF Salesforce Lightning application, including the home page, compliance dashboard, application view, request and task pages. Set up security controls, automated testing and Salesforce–ServiceNow integration logging. October Delivery Pack.
November 2026	**CAF Workflow & Integration Development.** Develop the approver queue, guided attestation, evidence handling, notifications and Sync Health functionality. Complete Salesforce–ServiceNow integration testing covering requests, tasks, approvals, evidence and status updates. November Delivery Pack.
December 2026	**CAF Reporting, ETL Testing & UAT.** Enhance compliance reporting, trend history and application views. Perform end-to-end ETL/integration testing, including data synchronisation, source-to-target validation, evidence transfer and reconciliation. Complete Customer UAT Cycles 1 and 2. December Delivery Pack.

October progress against plan (to 24 October)

October deliverable	Position
UX workshops and wireframes	No record in the repository
Home page	`cafHome`: five KPI tiles, each linking to the screen behind it (CAF-224, PR #44)
Compliance dashboard	Grid with search, needs-attention filter, totals, saved preferences; Approvals, Reports and Admin screens (CAF-233, CAF-27)
Application view	Not started. Planned enhancement in December
Request and task pages	Task record page with status path, due countdown and Start; request record page with task timeline (CAF-229, CAF-230)
App shell	CAF Compliance Lightning app, navigation, Controls tab, tab icons, Overdue and Awaiting attestation list views (CAF-222, CAF-226)
Security controls	CRUD and field-level security (CAF-220, deployed); CAF Viewer, Owner and Approver permission sets with server-side action checks (CAF-221, merged)
Automated testing	Apex suites with mocked callouts; 133 offline LWC unit tests; check-only validation against the org
Integration logging	Every ServiceNow callout logged to `CAF_Integration_Log__c` through a platform event (CAF-218); system-mode log write fixed 21 Oct
ServiceNow data	Tier 2 High Availability relationships activated and requests raised; 54 business apps added to CAF with owners; dashboard scoped to apps in CAF

October deliverable	Position
October Delivery Pack	Due at month end

Carried into November and December

#	Item	Why	Month
1	Deploy CAF-217 to the Salesforce org and assign the new permission sets	Home page, app shell and record pages are merged but not live	Early Nov
2	Named approver and approval notifications	Audit trail records only `sf.integration`; notifications never fire	Nov
3	Execute the pending write-path integration cases	Held back by decision; the harness already exists	Nov
4	Fix callout logging for non-admin users	Two Apex tests show no log row when a CAF user calls out	Nov
5	Assignee, instructions and tier pushed from ServiceNow (CAF-232, CAF-233)	Needed for My Work, the utility bar, control instructions and tier filters	Nov
6	Application view; trend history	Planned December reporting enhancements	Dec

6. Q4 · January – March 2027 (plan)

Q4 **Defects, production readiness and handover** · planned

Month	Planned work and milestones
January 2027	**CAF Defect Resolution & Regression Testing.** Resolve UAT and integration defects and perform regression testing across Salesforce and ServiceNow. Validate dashboards, requests, tasks, evidence, attestation, APIs, Sync Health and data integrity. Update technical and testing documentation. January Delivery Pack.
February 2027	**CAF Production Readiness & Integration Hardening.** Complete Salesforce and integration improvements, error handling, monitoring, security validation and synchronisation controls. Perform ETL/integration regression, re-synchronisation, API and data reconciliation testing. February Delivery Pack.
March 2027	**CAF Final Validation & Handover.** Complete final end-to-end Salesforce–ServiceNow testing, data reconciliation and defect closure. Finalise technical and testing documentation, complete knowledge transfer, Customer UAT sign-off, acceptance and system handover. Final CAF Delivery Pack and Project Closure by 31 March 2027.

Known items mapped to Q4

#	Item	Why	Month
1	Apex test class for `CafSyncHealth`	The only Apex class without tests; org coverage is 65% against the 75% production requires	Jan
2	Queued delivery with retry	A ServiceNow outage currently fails the user's action	Feb
3	Scheduled Sync Health with alerting; bulk-push resilience	Drift is found only when someone looks; 14 task pushes were lost in one bulk load on 21 Oct	Feb
4	JWT bearer for outbound authentication	Client credentials were a recorded deviation; JWT is the production target	Feb
5	Row-level security and Experience Cloud site	Deferred for the proof of concept; needed to realise the licensing benefit	Feb
6	Production deployment, knowledge transfer and handover	Closure by 31 March 2027	Mar
